1st & Final Bill

M. A. R. 57 (Rule 116)
Measurement Book

No. B

354660

Serial No. .....

Name of Work Remodelling of secondary drain on 3rd cross Siddappa layout in From..... To.....

Name of Contractor of nature of Agency Ward No. 8 Kodigehalli - V. Ramesh

Date of commencement of work Date:- 10/11/2022

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Job code:- 008-23-000002 Indent NO :- 53021 Work order NO :- BBMP/EE/BTP/WO/68/2022-23 AS NO :- AS/CE/(YNK) 17/2022-23 Date:- 20-08-2022 TS NO :- TS/CE/(YNK) 55/2022-23 Date:- 20-08-2022 Est. cost :- 40.00 Lakhs. Measurement Recorded on 28/12/22 1) Dismantling of flexible pavements and disposal of dismantled materials and Stacking serviceable and unserviceable						

Byatarayanapura

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	materials Separately - manual means Bituminous Course						
	Qty vide E-MB Page NO: 1 - - - - -					17.35	Cum
	@RS 1116.77 - - - - -					= RS	19375.95
	2) Dismantling of flexible Pavements and disposal of dismantled materials and stacking Serviceable and unserviceable materials Separately - manual means.						
	Qty vide E-MP Page NO: 01 - - - - -					88.71	Cum
	@RS 787.63 - - -					=	69870.65
	3) Earthwork Excavation by manual means of drains Canals, Water weirs, draft, approach channels key trenches, foundation of bridge and Such Et.						

M. A. R. 57 (Rule 116)
Measurement Book

No. B 354661

No. .....
of Work ..... From..... To.....
of Contractor of nature of Agency .....
f commencement of work .....

Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	Number	Length	Breadth	Depth		
2	3	4	5	6	7	8
Qty. vide	E-MB	Page No 1	-	-	397.37	Cum
	@ RS	214.80	-	-	=	85,355.07
Dismantling of existing structures like culverts, bridge,						
retaining wall's and other structures comprising of						
machinery, cement concrete, wood work, steel work etc.						
Qty vide	E-MB	Page No. 02	-	-	62.43	Cum
	@ RS	2140.01	-	-	=	133600.82
Providing and laying in position reinforced cement						

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Concrete for all sub structures of all buildings, irrigation work, sub structure works of bridges etc.						
	Qty vide E-MB page No:-02	-	-	-		30.45	cum
	@6841.87	-	-	-		=	208395.84
6)	Providing coursed rubble masonry (first sort) with hard stones in foundation and plinth with mortar 1:6						
	Qty vide E-MB page No:-02	-	-	-		54.81	cum
	@RS 6480.08	-	-	-	-	=	355173.15
7)	Removing and resetting of footpath slab/ remai and Refixing 225mm thick slabs.						

M. A. R. 57 (Rule 116)
Measurement Book

No. B 354662

Serial No. .....
Name of Work ..... From..... To.....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Qty vide E-MB Page No:- 02	-	-	-	-	27	Sqm
	@RS 246.72	-	-	-	-	=	6661.44
						=	
8)	Providing and fixing Pre-cast covering slab 25omm thick made out of RCC 1:2:4 & Jelly 20mm down side.						
	Qty vide E-MB Page No:- 03	-	-	-	-	277.50	cum
	@RS 5688.35	-	-	-	-	-	15,78,517.12
						=	
9)	Removing and Refixing slabs.						
	Qty vide E-MB Page No:- 03	-	-	-	-	2.57	Sqm.
	@RS 246.72	-	-	-	-	-	634.07

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	10) Providing and fixing Precast Covering Slab made out of CC 1:2:4 with 10 cm thick and finishing etc.						
	Qty vide E.M.B Page No:-03					0.28	Sq.m
	@ Rs 2017.90						565.01
	11) Providing Laying spreading and Compacting graded Stone aggregate to wet mix Macadam Specification including premixing the material with water at OMC etc.						
	Qty vide E-MB Page No:-03					14	Cum
	@ Rs 2764.8						38707.20
	13) Providing and fixing steel work in built up tabular						

M. A. R. 57 (Rule 116)

Measurement Book

No. B

354663

erial No. .....

ame of Work ..... From..... To.....

ame of Contractor of nature of Agency .....

ate of commencement of work .....

ate	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
	2	Number 3	Length 4	Breadth 5	Depth 6	7	8
	Round, square, rectangular, hollow tubes, trusses etc. qty vide E-MB Page No:-04 @RS 127.03	- - -	- - -	- - -	- - -	7018.35 kg =	891541.00
	(4) loading and unloading of stone boulders/stone aggregates/sand/kankar/moorum. qty vide E-MB Page No:-04 @RS 85.46	- - -	- - -	- - -	- - -	565.86 =	48358.39

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	15) Cost of haulage excluding loading and unloading taking output 18t and lead of 10km						
	Ref vide E-MB page No:-04	-	-	-	-	724.30	t.km
	@ RS 121.26	-	-	-	-	=	87828.61
					Total	=	3524584.35
					G.S.T @ 18%	=	634425.18
					Grand total	=	4159009.53
					Round off		4159010.00

Certificate:-

1) Certified that the work done is satisfactorily.
2) There is no departmental issues by BBMP
3) The agency has cleared the debris from the work spot.

21/12/22

Assistant Executive Engineer
Kodigehalli Sub Division

M. A. R. 57 (Rule 116)
Measurement Book

No. B 354664

erial No. .....
ame of Work ..... From..... To.....
ame of Contractor of nature of Agency .....
ate of commencement of work .....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
	2	3	4	5	6	7	8

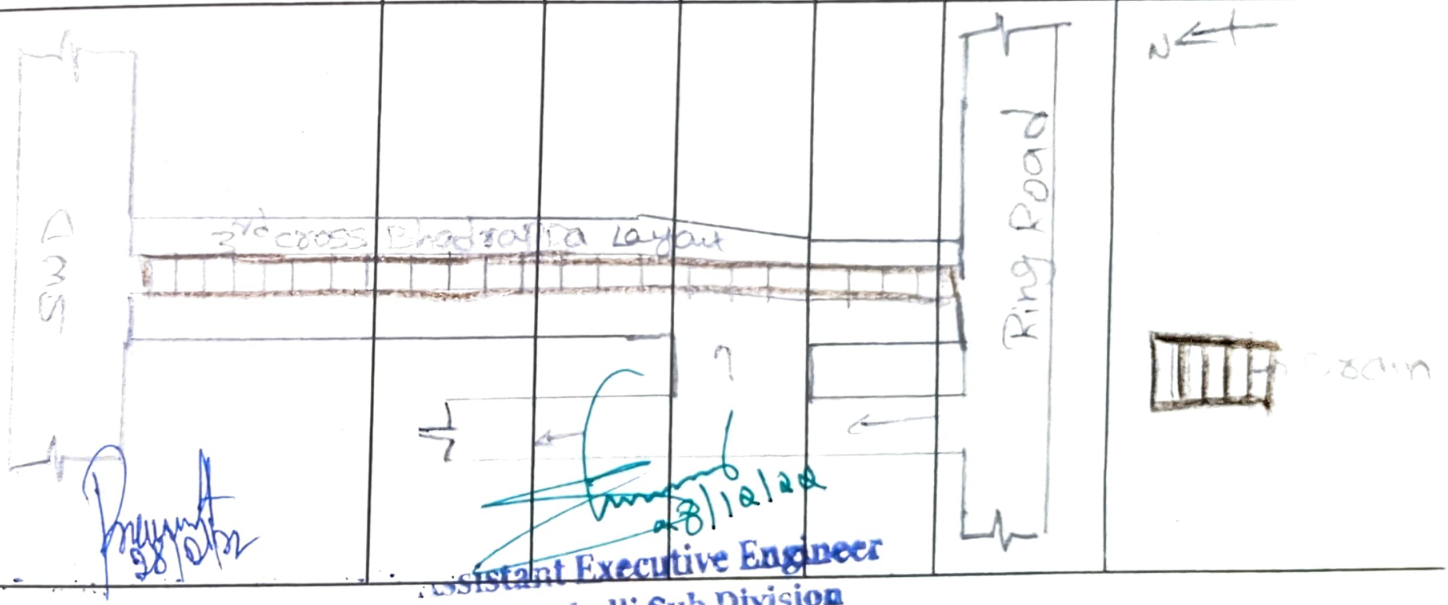

1st & final

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	P 3726						
	ಲೆಕ್ಕಶೀರ್ಷಿಕೆ Zonal public Works - Pow works ರಡಿ						
	ಒಟ್ಟು ಮೊಬಲಗು ರೂ. 4159000/- ಖರ್ಚು ಮಾಡಿದೆ						
	ಇದರಲ್ಲಿ ರೂ. 182000/- ಗೆ ಮಿತಿಯಾಣತೆ						
	ಮೊದಲೊಂದು ರೂ 3977000/- ಗಳನ್ನು						
	[illegible]						
	[illegible]						
	[illegible]
